





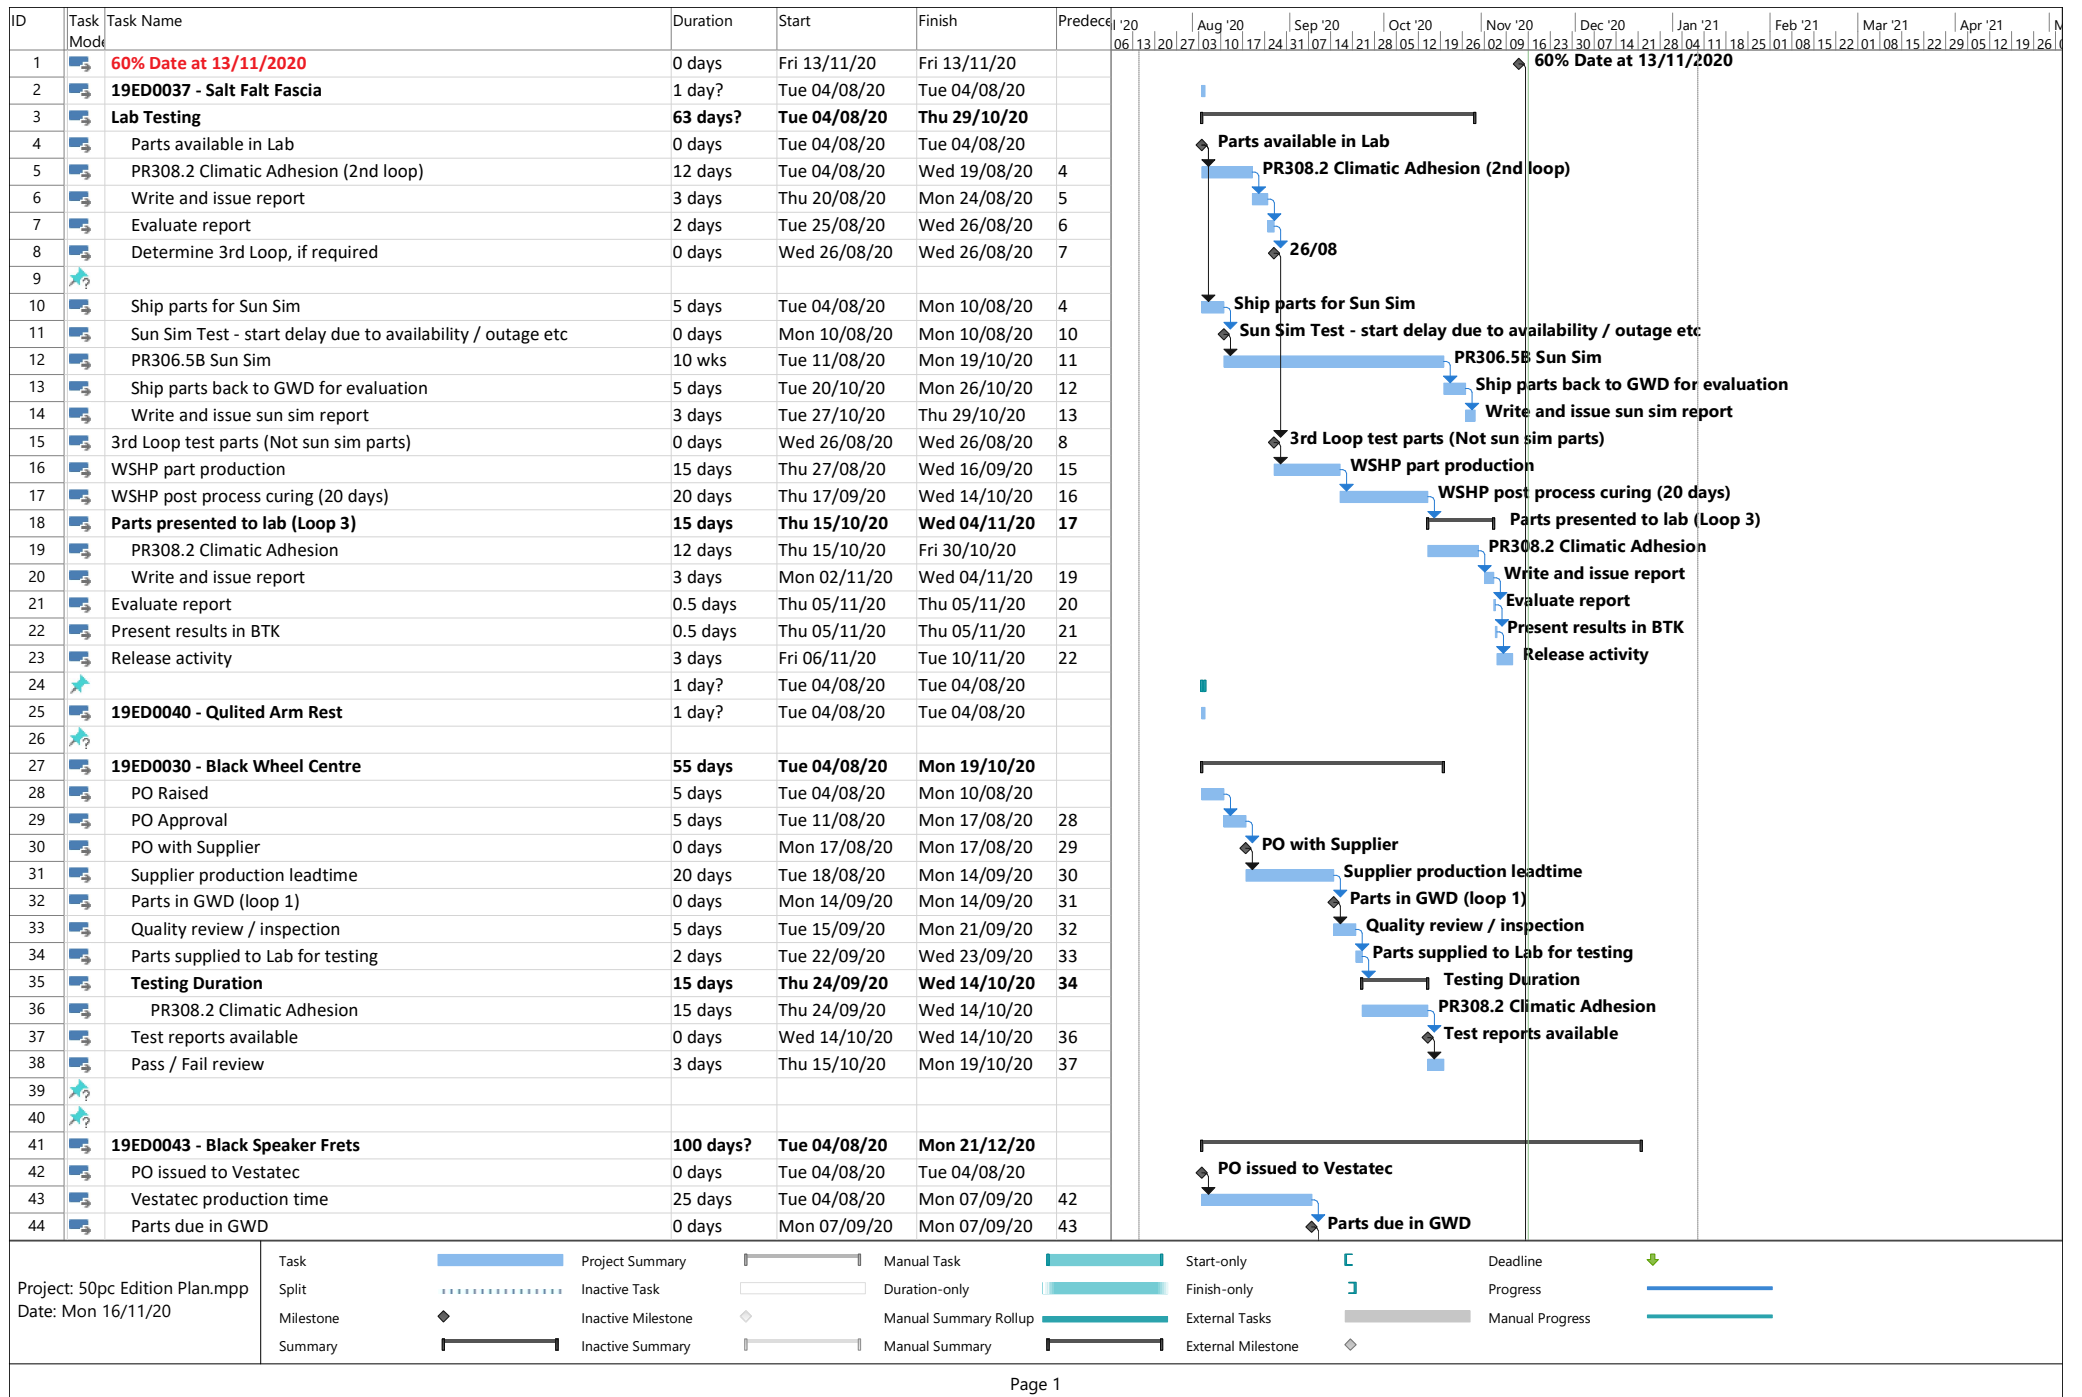

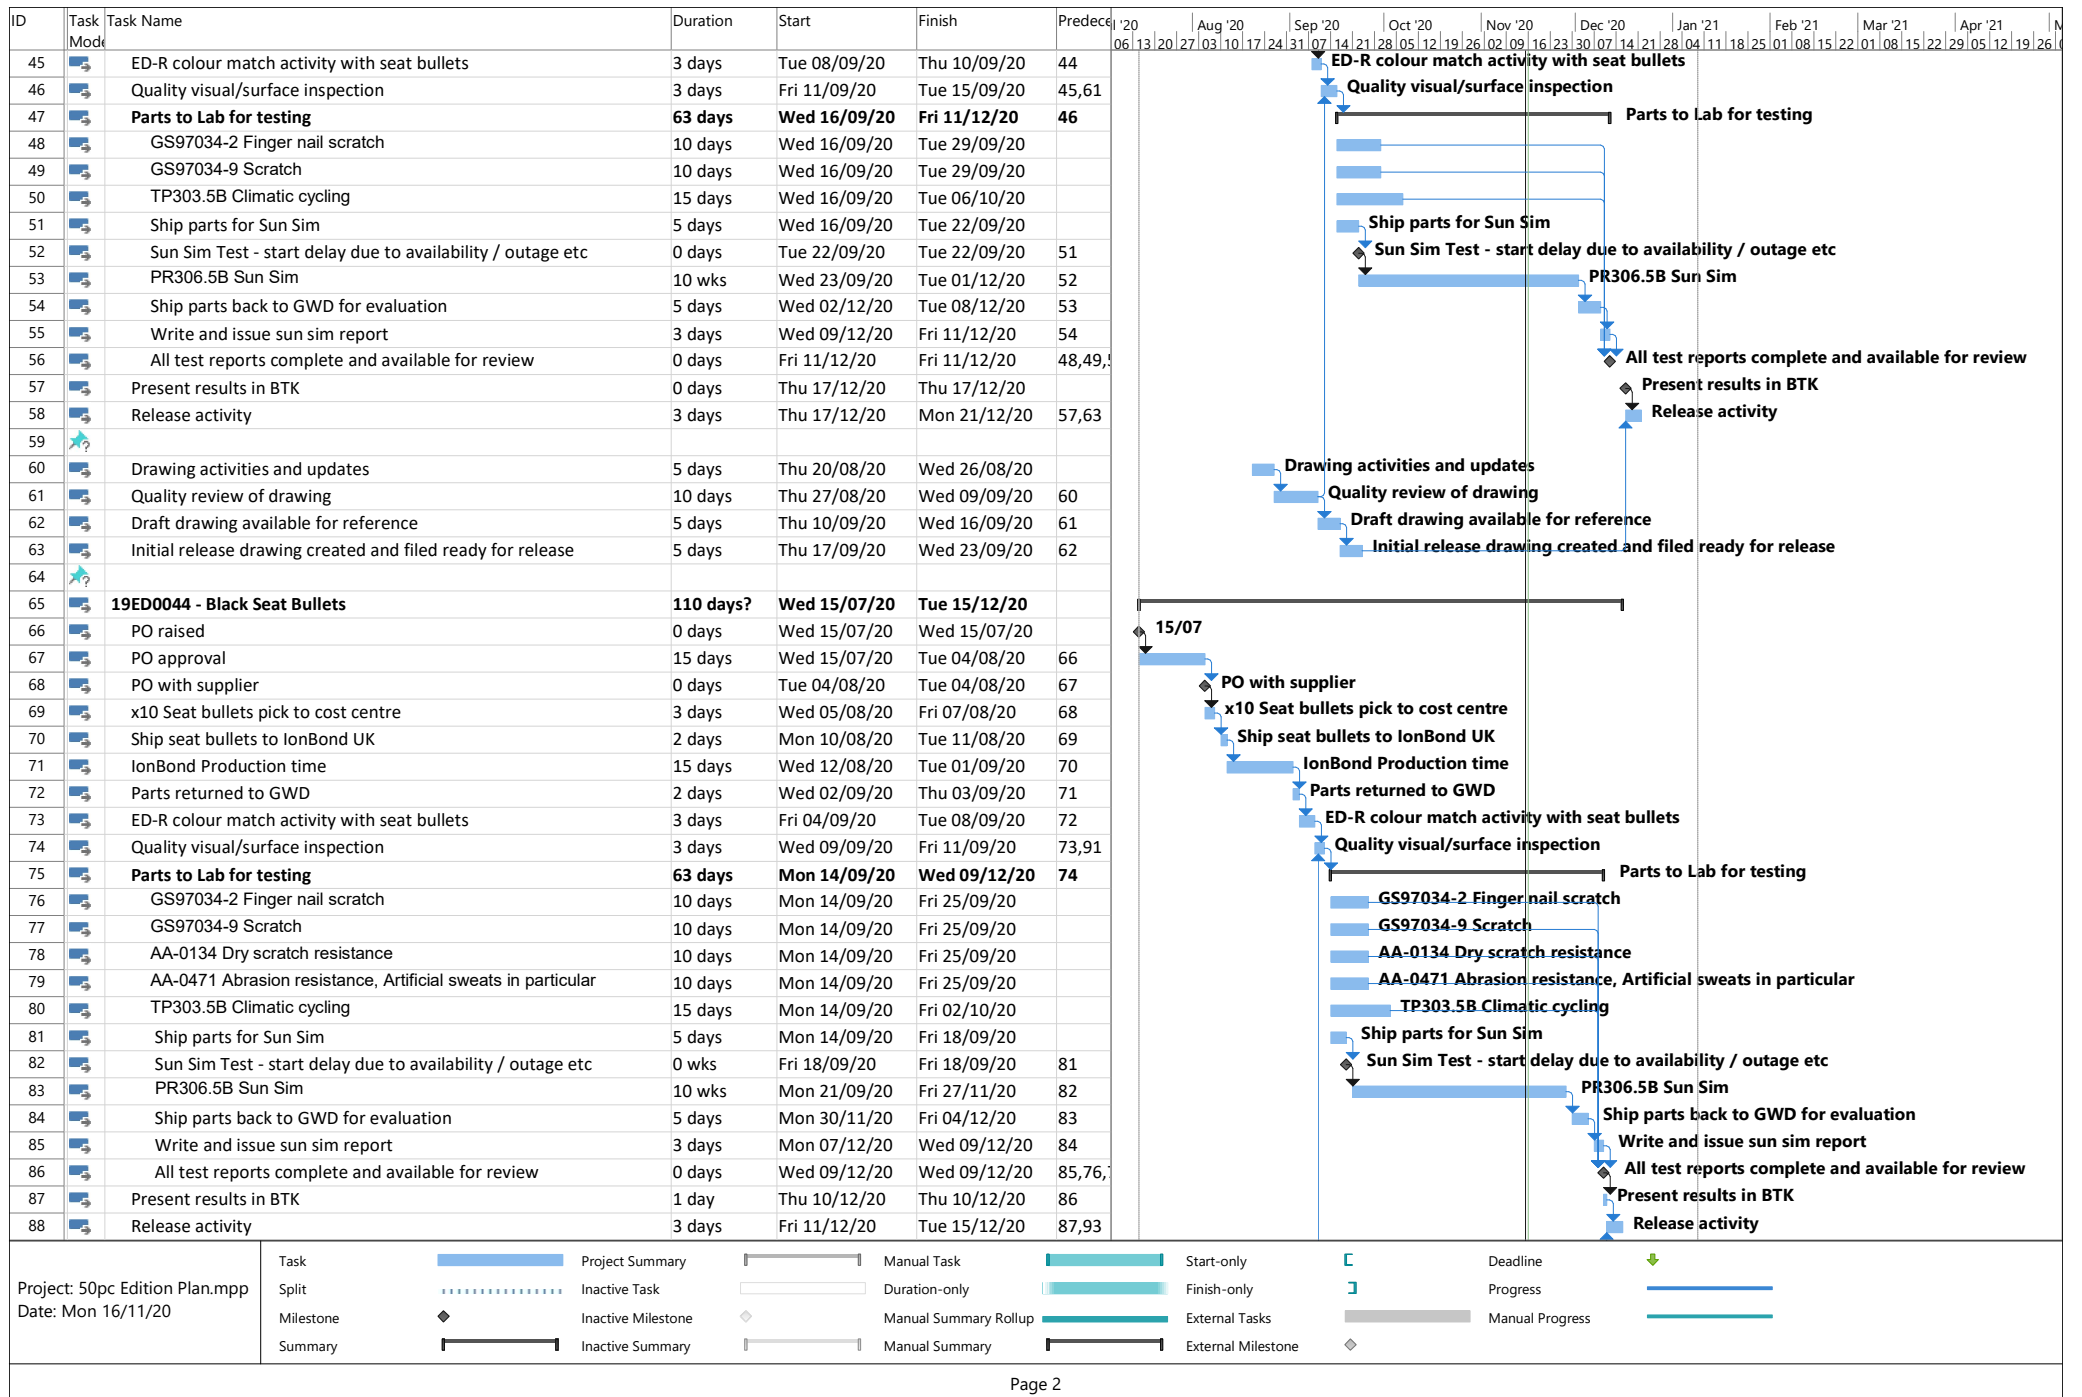

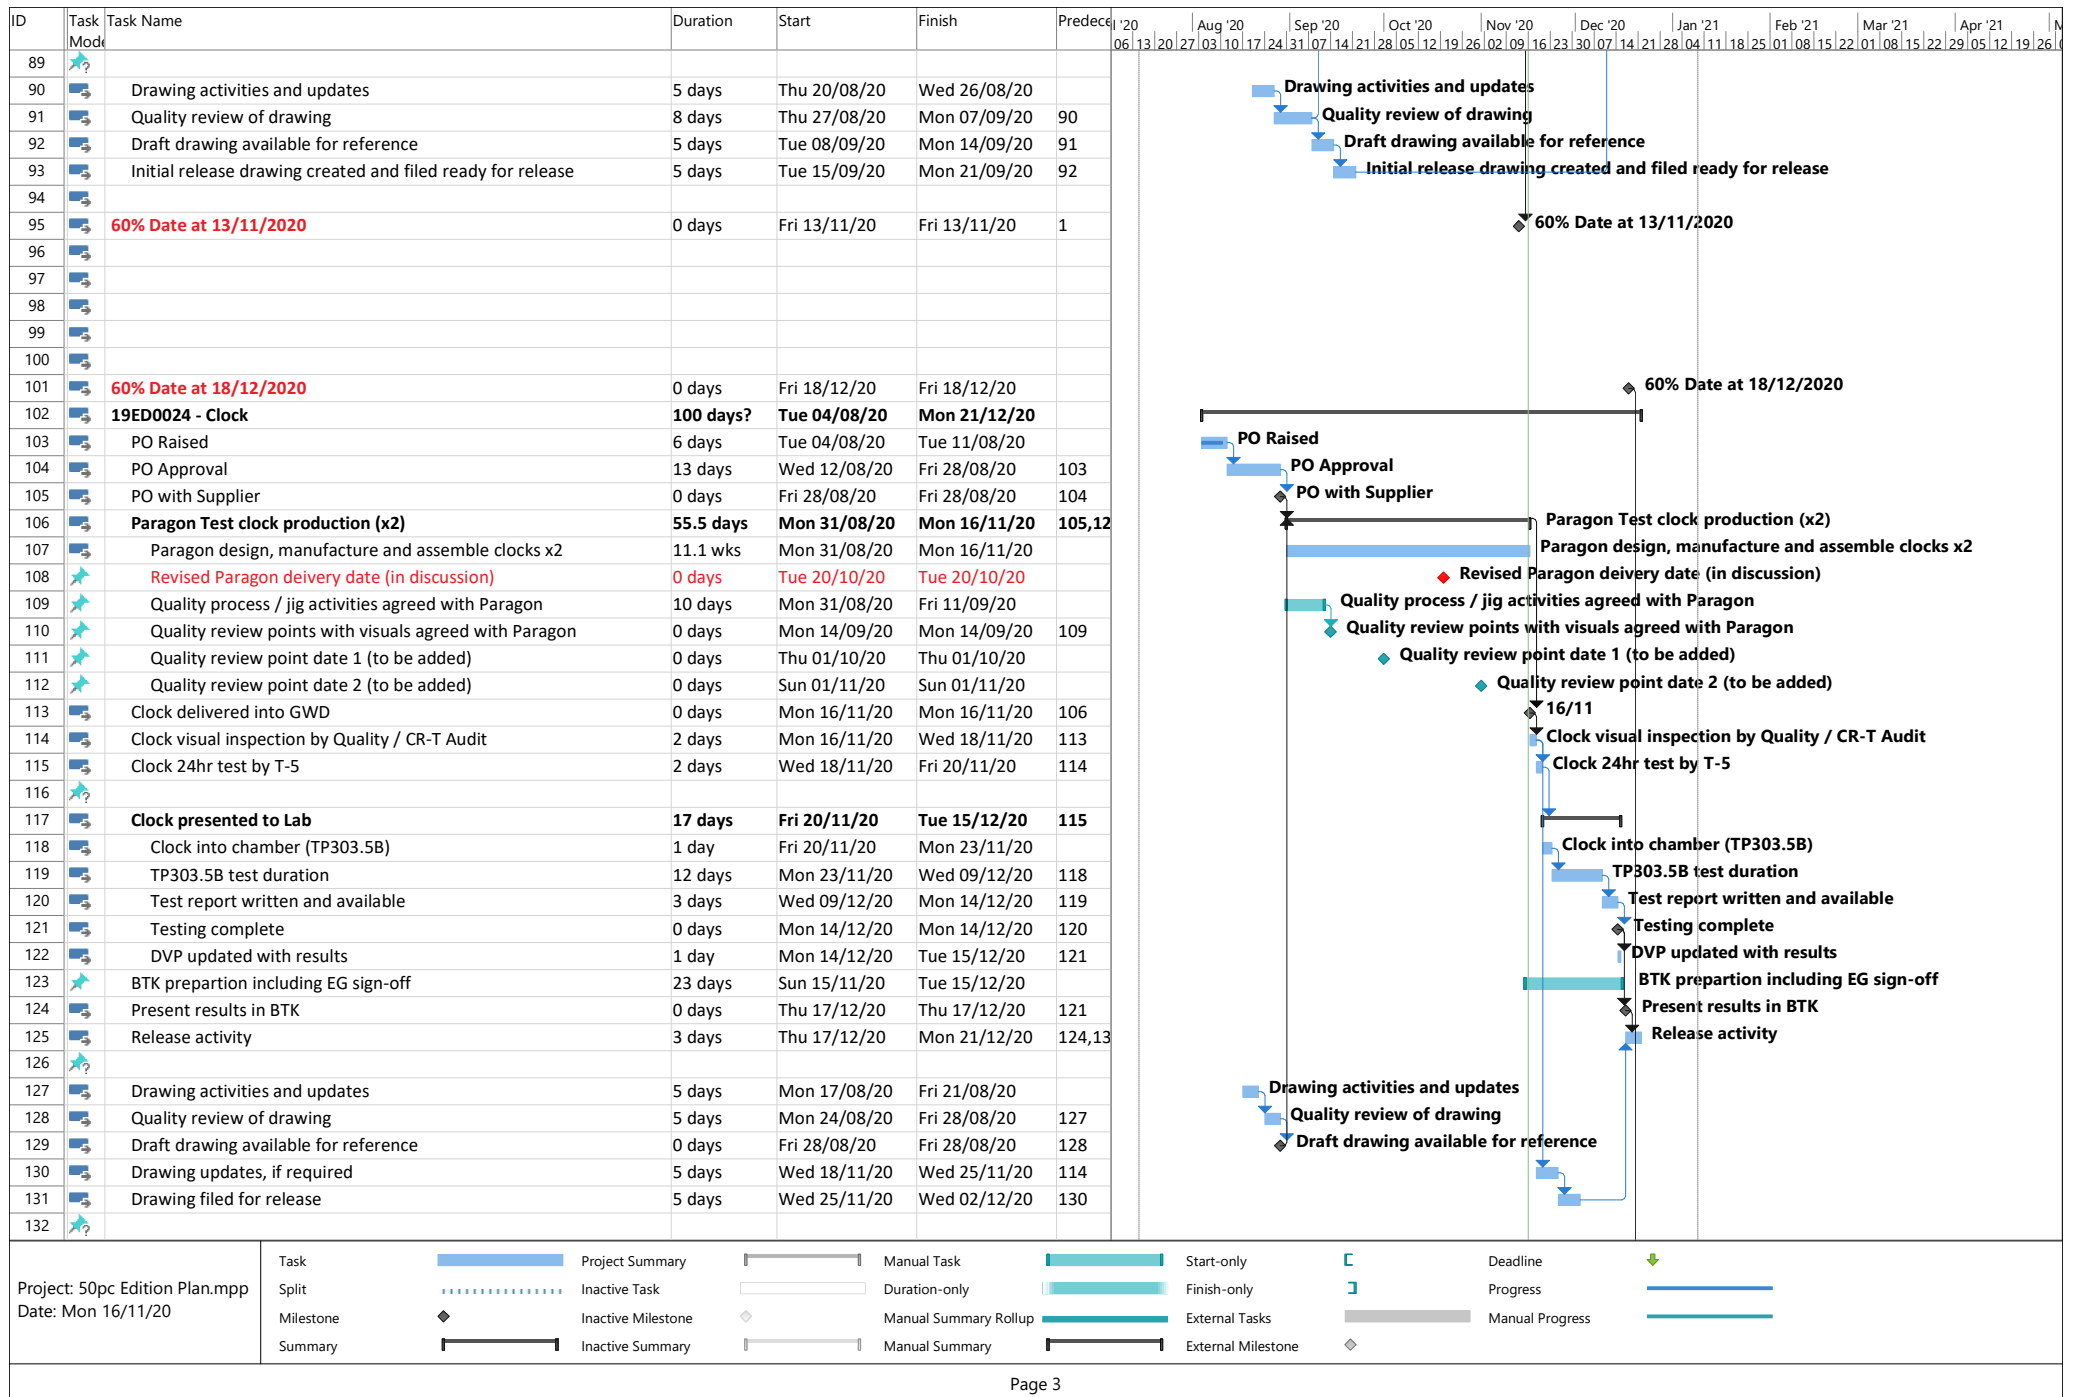


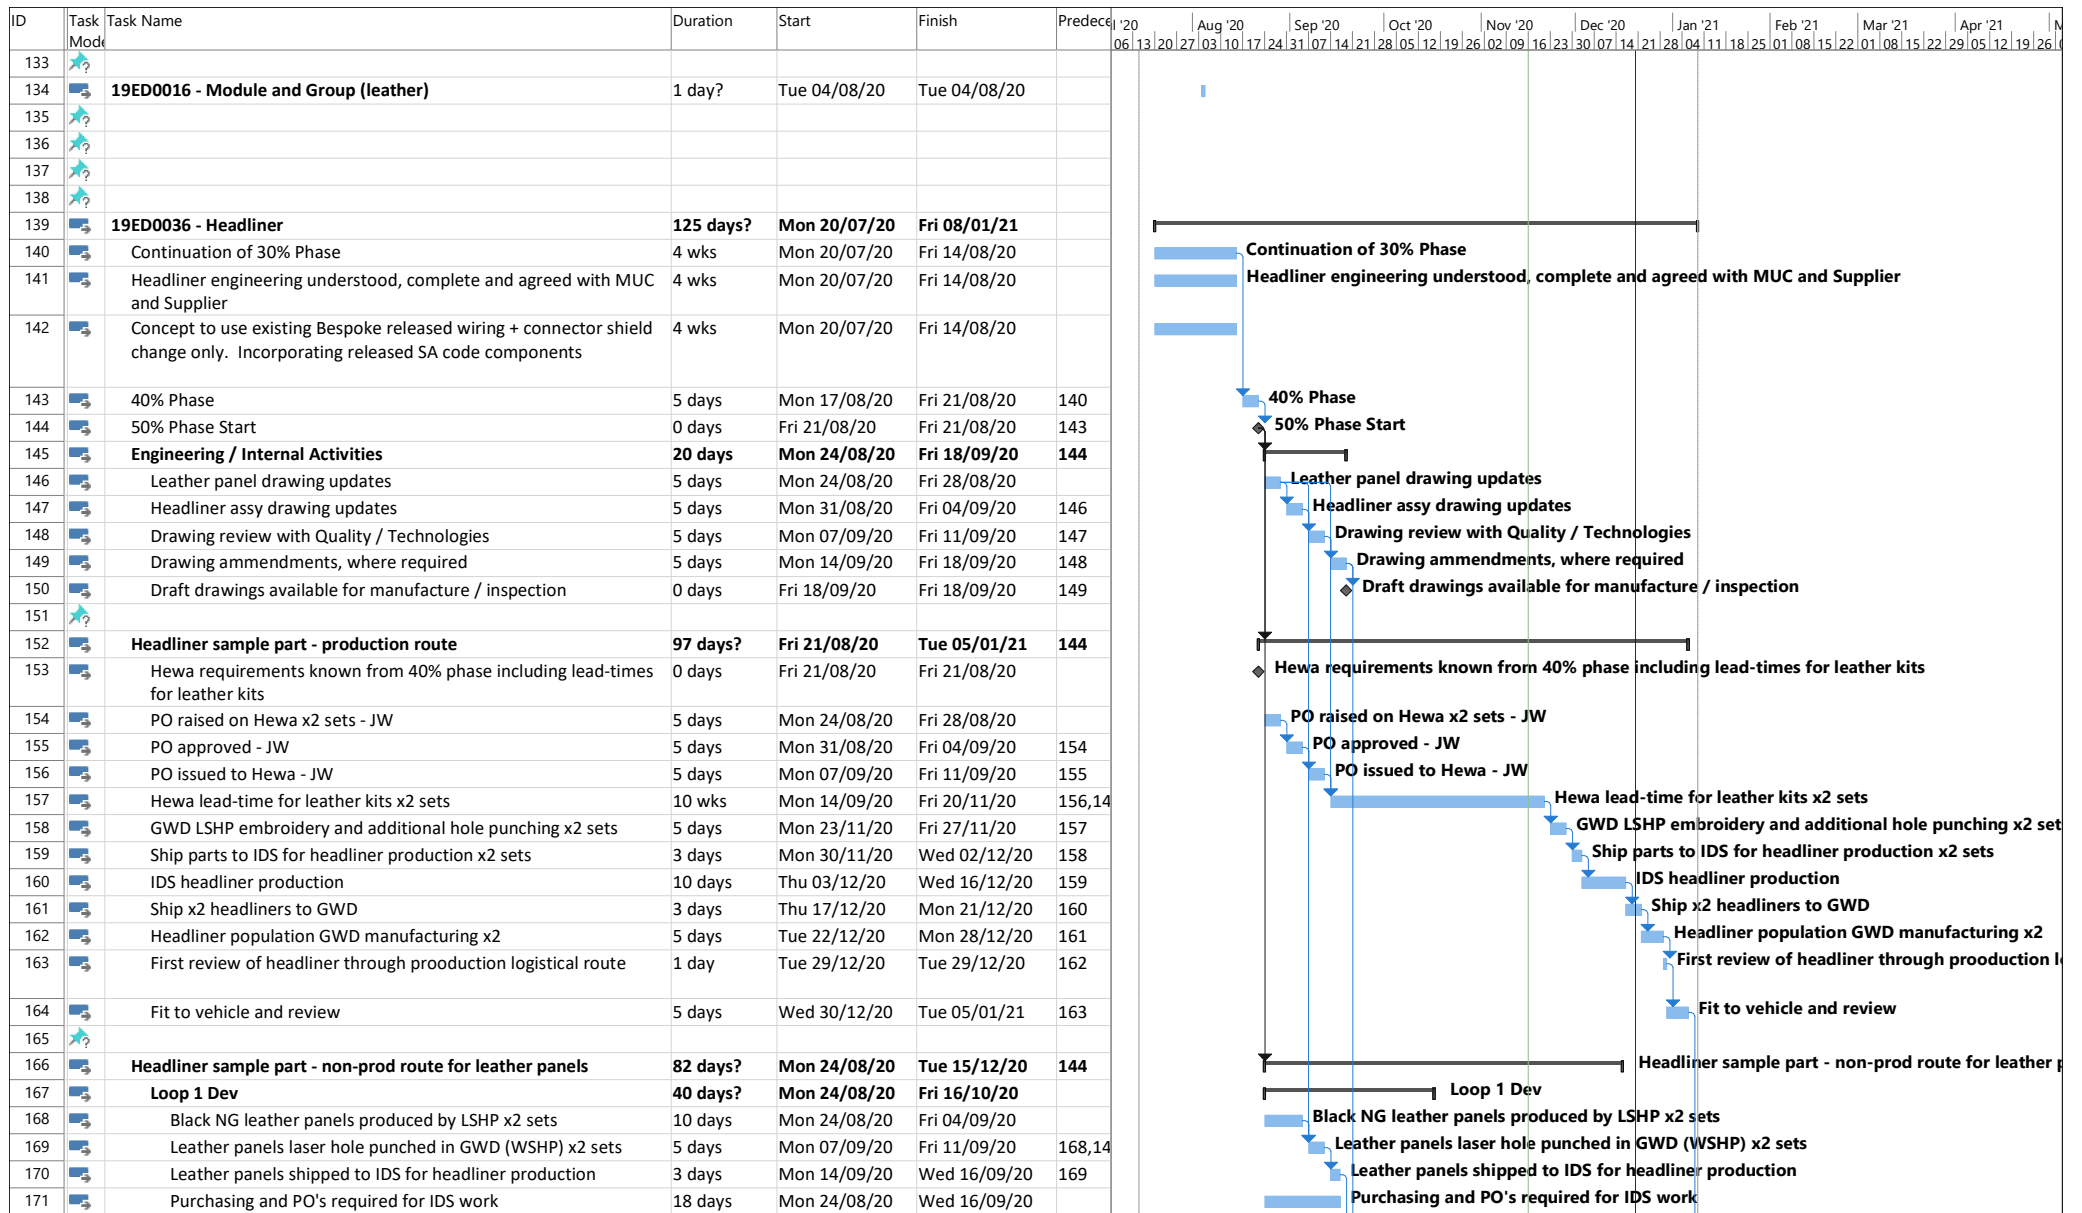

Project: 50pc Edition Plan.mpp
Date: Mon 16/11/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	Jul '20	Aug '20	Sep '20	Oct '20	Nov '20	Dec '20	Jan '21	Feb '21	Mar '21	Apr '21	May '21
172	🚚	Parallel IDS / Eng / Quality activities (telcos etc) to support iDS production work	18 days	Mon 24/08/20	Wed 16/09/20												
173	🚚	Quality supplier and process development	18 days	Mon 24/08/20	Wed 16/09/20												
174	🚚	IDS headliner production	10 days	Thu 17/09/20	Wed 30/09/20	170											
175	🚚	Ship x2 headliners to GWD	3 days	Thu 01/10/20	Mon 05/10/20	174											
176	🚚	Quality / ED-R review of hole positions on stitched headliners (seam positioning etc)	2 days	Tue 06/10/20	Wed 07/10/20	175											
177	🚚	Headliner population - GWD manufacturing x2	5 days	Thu 08/10/20	Wed 14/10/20	176											
178	🚚	Review of headliner illuminated - ED-R / Team	2 days	Thu 15/10/20	Fri 16/10/20	177											
179	🔍?																
180	🚚	Loop 2 Dev	42 days	Mon 19/10/20	Tue 15/12/20	178											
181	🚚	Product development updates for star positions relative to seam edges etc, as required	2 days	Mon 19/10/20	Tue 20/10/20												
182	🚚	Black NG leather panels produced by LSHP x2 sets	10 days	Wed 21/10/20	Tue 03/11/20	181											
183	🚚	Leather panels laser hole punched in GWD (WSHP) x2 sets	5 days	Wed 04/11/20	Tue 10/11/20	182											
184	🚚	Leather panels shipped to IDS for headliner production	3 days	Wed 11/11/20	Fri 13/11/20	183											
185	🚚	Purchasing and PO's required for IDS work	18 days	Mon 19/10/20	Wed 11/11/20												
186	🚚	Parallel IDS / Eng / Quality activities (telcos etc) to support iDS production work	18 days	Mon 19/10/20	Wed 11/11/20	176											
187	🚚	Quality supplier and process development	18 days	Mon 19/10/20	Wed 11/11/20												
188	🚚	IDS headliner production	10 days	Mon 16/11/20	Fri 27/11/20	184											
189	🚚	Ship x2 headliners to GWD	3 days	Mon 30/11/20	Wed 02/12/20	188											
190	🚚	Quality / ED-R review of hole positions on stitched headliners (seam positioning etc)	2 days	Thu 03/12/20	Fri 04/12/20	189											
191	🚚	Headliner population - GWD manufacturing x2	5 days	Mon 07/12/20	Fri 11/12/20	190											
192	🚚	Review of headliner illuminated - ED-R / Team	2 days	Mon 14/12/20	Tue 15/12/20	191											
193	🚚		1 day?	Tue 04/08/20	Tue 04/08/20												
194	🚚	BTK Activities, based on carry-over electrical concept and no testing (ready for release)	20 days	Mon 21/09/20	Fri 16/10/20	149											
195	🚚	Release activity (only achieved after production intent part reviewed)	3 days	Wed 06/01/21	Fri 08/01/21	194,16											
196	🚚																
197	🚚	60% Date at 18/12/2020	0 days	Fri 18/12/20	Fri 18/12/20	101											

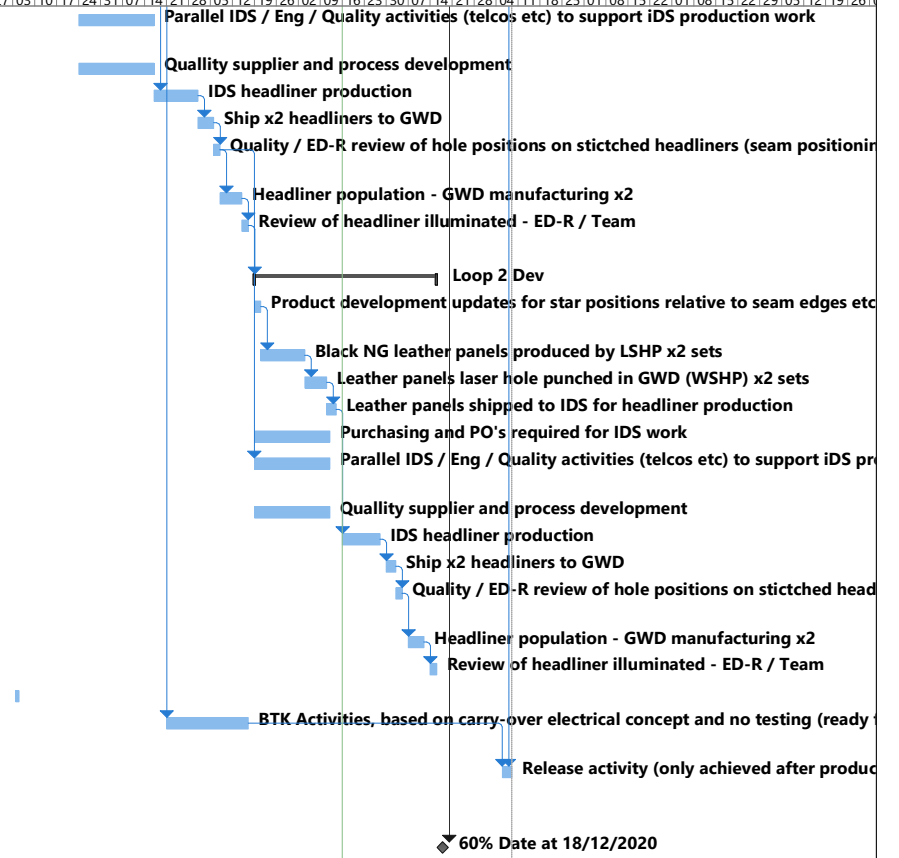

Project: 50pc Edition Plan.mpp
Date: Mon 16/11/20

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
